

Course: Individual Software Development Process' 2026

Iteration Report: Iteration 1

By **COOKIN'BYDOING**

Chosen Irl Challenge: Project B: Lab Workflow & Request Management

Thanathas Puttapipat	6810545638
Anawin Chaichana	6810545964
Hugh Jaiden	6810546006
Thichanon Kangkachit	6810545611
Hugo Desvignes	6810546715


Table of Contents

1. Project Snapshot.....	1
1.1 Project-Wide Gantt Chart.....	1
1.2 Current Iteration Gantt Chart.....	1
2. Sprint/Board Status Snapshot.....	1
3. Scope Addition/Change Log.....	2
4. Retrospective.....	2
5. Testing & Quality Notes.....	2
6. Project Risk Register.....	3
7. Individual Contribution Log.....	3

1. Project Snapshot

Project Repository : (WIP)

1.1 Project-Wide Gantt Chart

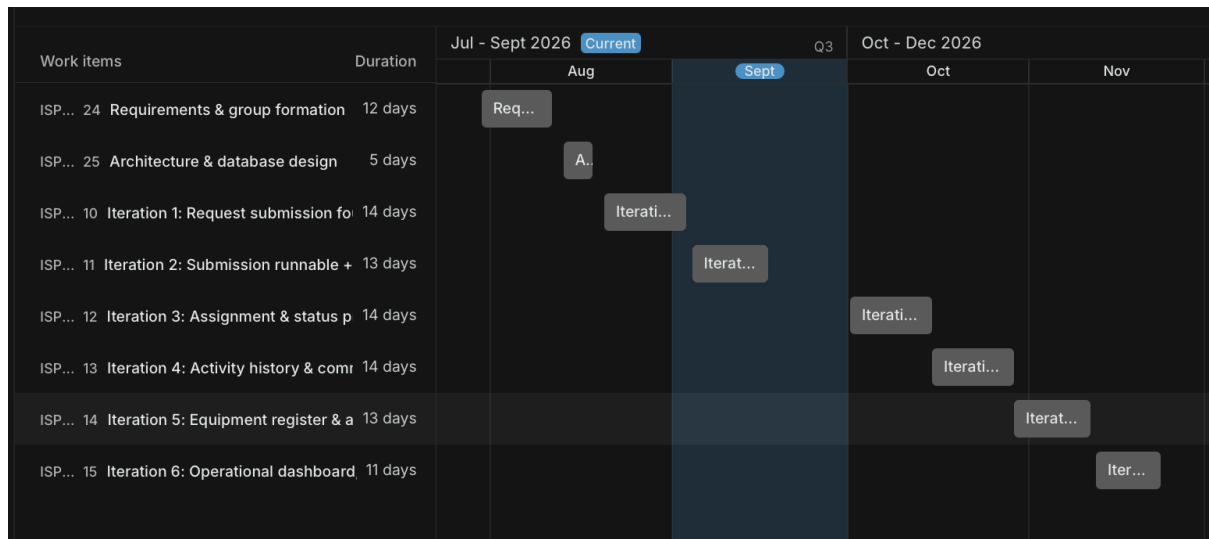

Critical Path: Requirements sign-off → Architecture/DB schema finalisation → Request submission implementation (US-1) → Request management & assignment (US-3) → Activity history (SG-4) → Deployment

Critical Path Duration: 108 calendar days

1.2 Current Iteration Gantt Chart



Critical Path: Docker Compose stack → Request/user/status schema → Submit form & validation (US-1) → Schema review against SRS-1 to SRS-4

Critical Path Duration: 9 calendar days

2. Sprint/Board Status Snapshot

Iteration Goal: Establish the foundation for the request-submission slice, containerised environment, database schema, and interface design so that lab members can submit and track requests and the lab manager can view all incoming requests, replacing the current email/chat channel. Supports Sub-Goals SG-1 and SG-2. *This iteration targeted the design and environment foundation and a runnable slice was not achieved and is carried into Iteration 2.*

Capacity Declared: 2 user stories. Iteration 1 permits up to 3, but the team declared 2 because this is the first iteration with no velocity baseline, and a significant share of the iteration is absorbed by non-story setup work (containerised environment, database schema, repository structure) that must exist before any story can be demonstrated. US-3 is scoped to its read-only half for the same reason.

User Story	Description	Owner	Status	Within Capacity (Y/N)	Notes
US-1	As a lab member, I want to submit a request and track it, so I can get what I need for the lab	Hugo Desvignes	In-Progress	Y	Sliced to submission + own-request list (SRS-1 to SRS-4). Equipment register/edit deferred to a later iteration as it belongs to SG-5. Required the request/user/status schema and attachment volume, which were built as part of this story
US-3	As a lab manager, I want to be able to view and assign lab requests to TAs	Thichanon Kangkachit	In-Progress	Y	Read-only overview of all requests delivered (status, owner, priority). Assignment and status-change logic (SRS-6) deferred to Iteration 2. Blocked on US-1 schema for the first three days

3. Scope Addition/Change Log

Item added/changed	Reason	What as dropped to compensate (one-in-one-out)
Add status for request "Review"	We need review status to notify the lab manager to review the result and either accept or reject it.	None required to drop. The "Review" status was added as a single value in the existing request status field, with no additional screens or logic in this iteration.

4. Retrospective

What went well	What didn't go well	Action items for next sprint
Containerised environment was agreed early, so every member is working against the same MySQL version and application runtime rather than their own local install	No runnable path was produced, so nothing could be informally tested and three of five members had only design work to demonstrate	Deliver one working submit → save → display slice in the first three days of Iteration 2, before any new story work begins
Ownership was agreed per component up front, so no two members duplicated work	Team underestimated how much of the iteration setup would absorb, leaving no room for a demoable feature	Declare Iteration 2 capacity from measured time per item this iteration rather than from estimate
Design review surfaced schema before any code was written, avoiding rework later	The iteration goal of a demoable was not met; only design and environment work was delivered	Build one feature that actually works from start to finish at the beginning of Iteration 2, instead of leaving it until the end.

5. Testing & Quality Notes

No executable testing was performed this iteration, as the work produced was design and environment rather than a runnable path. Each member reviewed their own component

Database design Expectation vs Reality (Hugo Desvignes)

When designing I created some unnecessary tables , and didn't foresight simplicity over reality , in fact in the real design we didn't need that many tables

By doing the diagram we could discuss and pinpoint the mistakes made in my understanding of the project

Containerisation (Hugh Jaiden)

At first we used volumes and directly mounted the entire directory to the container, with the reasoning being that we shouldn't have to rebuild the container every time we change something. Later on we found out about Watch and implemented that instead.

Interface design review (Thichanon Kangkachit/PO)

We clarify and redesign some missing logic on the request management flags and visualize several pages such as the login page and the request management page which will be the main template reference for managing equipment and, perhaps, operational dashboard. Additionally, we make some visual guidelines on the interaction scenarios displayed such as when filling the request form, entering the request row which can view detail, activity history, and message log.

Planned Test in Future

	Test to perform	Expected Result
SRS-2	Submit a request with a required field left empty	Validation error shown; request not saved
SRS-3	Submit a valid request	Saved with a unique request ID and status "Pending"
SRS-4	Open a lab member's request list	Only that member's own requests listed, with current status

6. Project Risk Register

Risk ID	Description	Likelihood (L/M/H)	Impact (L/M/H)	Mitigation/Contingency	Status
R-01	No runnable build in Iteration 1, so schema and validation defects stay undetected	H	M	Deliver one working submit → save → display path in the first three days of Iteration 2	Open
R-02	Schema, interface and container stack were built in parallel and not yet integrated	M	H	Integrate all three on the shared Compose stack before starting new story work	Open
R-03	Only Hugh Jaiden can run and configure Docker, a single point of failure for the whole team	M	H	Pair Hugh Jaiden with <i>Anawin Chaichana</i> ; two members must bring the stack up independently	Open
R-04	No velocity baseline, so Iteration 2 capacity may be over-declared	M	M	Record actual time per backlog item this iteration and declare capacity from that figure	Open
R-05	Files are mounted at runtime rather than copied at build time, so the development container does not match a clean build; deployment may fail on issues not visible during development	M	M	Produce a build-based Compose configuration and verify the system against it before deployment	Open

7. Individual Contribution Log

Student Name	Tasks owned this sprint	Course concept(s) applied	Evidence	Self-rated effort (1-5)
Thanathas Puttapipat	Role-permission to interface visibility mapping; frontend design contributions to the request management and overall layout	Requirement traceability from role definitions (SRS-10, SRS-12) to interface visibility rules	Figma screens showing the page as each role sees it; video segment at 06:51	4
Anawin Chaichana	Repository initialisation and project setup; cross-checking and reviewing other members' work; iteration report authoring	Informal review applied to validate design against acceptance criteria before any build exists	Repository; Report section 1-4, 6; video segment at 04:48	4
Hugh Jaiden	System architecture decision; Docker Compose stack; onboarding all members onto the containerised environment	Development environment: containers vs bare metal; modular MVC architecture selection	<i>docker-compose.yml</i> ; video segment at 04:04	4
Thichanon Kangkachit	Request management page layout in Figma; overall web skeleton layout; added "Review" status to the request lifecycle	URS-3 → SRS-6 traceability from requirement to UI field; Apply Modular architecture separated web layout into smaller components to reduce coupling.	Figma file (page and skeleton layouts); Report section 3; video segment at 08:28	4
Hugo Desvignes	Database diagram for request/user/status; role-permission model	RDBMS vs NoSQL decision; mapped SRS-3 and SRS-10 into schema	UML diagram; video segment at 01:30	4
