Course: Individual Software Development Process' 2026

Iteration Report: Iteration 3

By COOKIN'BYDOING

Chosen Irl Challenge: Project B: Lab Workflow & Request Management

Thanathas Puttapipat	6810545638
Anawin Chaichana	6810545964
Hugh Jaiden	6810546006
Thichanon Kangkachit	6810545611
Hugo Desvignes	6810546715


Table of Contents

1. Project Snapshot..... 3
2. Sprint/Board Status Snapshot.....**4**
3. Scope Addition/Change Log..... **5**
4. Retrospective..... **5**
5. Testing & Quality Notes.....**6**
6. Project Risk Register.....**7**
7. Individual Contribution Log..... **8**

1. Project Snapshot

Project Repository : https://github.com/0n0w1n/Vase_Lab_Management

Current Iteration Gantt Chart

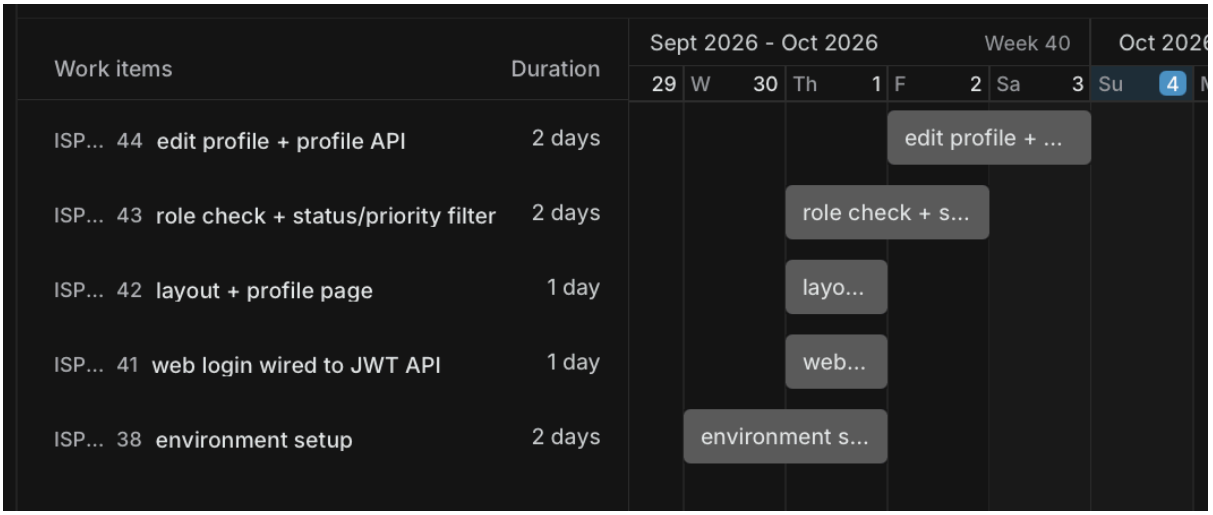

Critical Path:

The environment was setup then web login was connected with JWT API, after that the edit profile page was finished using login session

Critical Path Duration:

4 calendar days

2. Sprint/Board Status Snapshot

Iteration Goal: Linked authentication so that requests are attributed to, and filtered by, the signed-in user. Supports Sub-Goals SG-1 and SG-2. This was achieved in the first half of the iteration and demonstrated at the mid-term checkpoint; Furthermore, set up an additional profile page edition feature, for the user to edit name, password, and organisation.

Capacity Declared:

User Story	Description	Owner	Status	Within Capacity (Y/N)	Notes
US-1	As a lab member, I want to be able to submit a request, register and edit equipment, and track them, so I can get what I need for the lab.	Anawin	In-Progress	Y	SRS-4 is almost done, only left for linking with the history log, and only SRS-1 is on hiatus due to possible implementing complications.
US-3	As a lab manager, I want to be able to view and assign lab requests to TAs.scrum	Thichanon	In-Progress	Y	Staff see all request and can filter by status and priority.SRS7 in iteration 4
-	Profile Page (view and edit)	Thichanon, Hugo	Done	N	Not in the SRS.

3. Scope Addition/Change Log

Item added/changed	Reason	What as dropped to compensate (one-in-one-out)
Change app routing to be split into 2 folder which are (auth) and (main)	To separate the log in and logged in part.	Drop the old routing which is every route in app folder
Add profile page	To let user edit and see their profile; To display user role	Templated user profile

4. Retrospective

What went well	What didn't go well	Action items for next sprint
Work distribution is better	Within the given time we could have delivered more	Equipment management feature
Finalized product was better because we have more time	Handling the project at the same time as the flood crisis	Foundation of Request Management & Operational Dashboard
Overall communication improved	We still mainly merge without review (or with too little reviewers)	Implement Role Based permissions

5. Testing & Quality Notes

The n tests in Iteration 3 were run.

Test run

Test	Test to perform	Result
Profile page	Go to profile page and see if it appear	It appear and display user data properly
SRS-4	Only that member's own requests listed, with current status	The list reads live data and shows current status, and is filtered per user. Though it hasn't been linked the action with the history log
SRS-3	Sign-in member submit a valid request	PASS. The request is saved under the sign-in user
SRS-10	Login with a wrong password or wrong email	PASS. same message for both

6. Project Risk Register

Risk ID	Description	Likelihood (L/M/H)	Impact (L/M/H)	Mitigation/ Contingency	Status
R-01	Having a merge conflict	H	M	Coordinate changes and pull updates regularly. Resolve conflicts together and test before merging.	Open
R-02	Users may modify other users' profiles without permission.	M	H	Check user identity and permissions in the backend before allowing updates. Test unauthorized requests	Open
R-03	Frontend and backend may use incompatible API formats, causing features to fail.	M	H	Agree on API formats and test integration early. Fix incompatible endpoints before release.	Open
R-04	A team member may be unavailable, delaying assigned tasks.	M	M	Share documentation and progress regularly. Reassign urgent tasks to available members.	Open

7. Individual Contribution Log

Student Name	Tasks owned this sprint	Course concept(s) applied	Evidence	Self-rated effort (1-5)
Thanathas Puttapipat	Linked back-end Authorisation system with the login	CRUD	Commit fbde285	5
Anawin Chaichana	The access denied page when dont have access and status/priority filter	CRUD	Commit 4d5e075	5
Hugh Jaiden	Overseeing API modifications	CRUD	Commit cf3bc66	4/5
Thichanon Kangkachit	Design of Profile page and implement in front end	Modular Architecture	Commit c6caff5 , 74bc58a	5
Hugo Desvignes	Edit feature for the profile page improving dynamic routing and backend update request	CRUD , Design implementation	Commit `7c4c361`	5
