Course: Individual Software Development Process' 2026

Iteration Report: Iteration 5

By COOKIN'BYDOING

Chosen Irl Challenge: Project B: Lab Workflow & Request Management

Thanathas Puttapipat	6810545638
Anawin Chaichana	6810545964
Hugh Jaiden	6810546006
Thichanon Kangkachit	6810545611
Hugo Desvignes	6810546715


Table of Contents

1. Project Snapshot..... 3
2. Sprint/Board Status Snapshot.....**4**
3. Scope Addition/Change Log..... **5**
4. Retrospective..... **5**
5. Testing & Quality Notes.....**6**
6. Project Risk Register.....**7**
7. Individual Contribution Log..... **8**

1. Project Snapshot

Project Repository : https://github.com/0n0w1n/Vase_Lab_Management

Current Iteration Gantt Chart

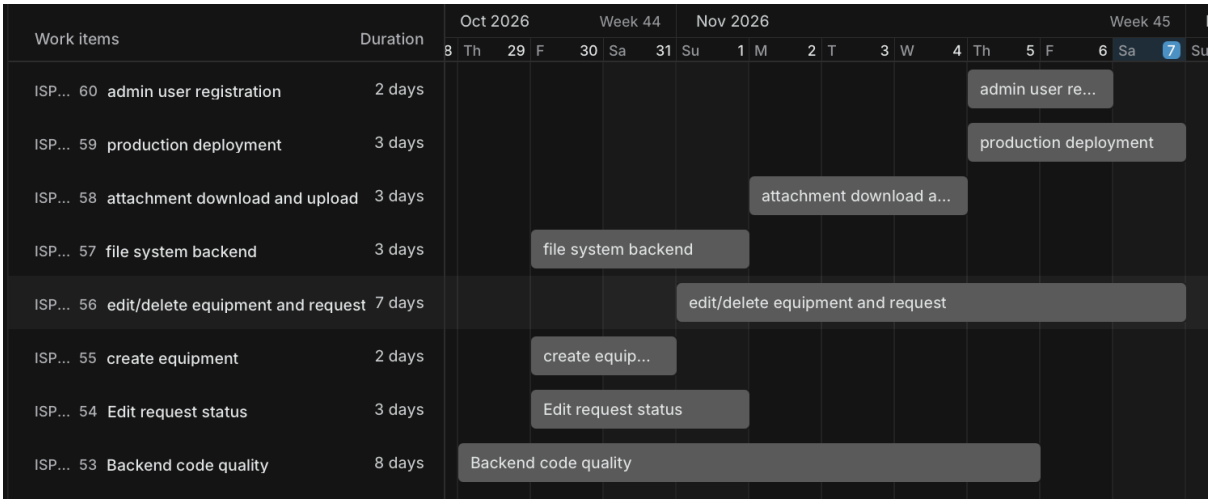

Critical Path:

Create Equipment → Edit/delete equipment and request

Critical Path Duration:

9 calendar days

2. Sprint/Board Status Snapshot

Iteration Goal: Let the lab members attach files to their requests and let staff manage the equipment register. In this iteration we delivered file upload and download on requests, creating equipment and status editing. and we start the production setup

Capacity Declared: 2 US and 3 additional works. We follow the action item from our iteration 4 retrospective

User Story	Description	Owner	Status	Within Capacity (Y/N)	Notes
US-1	As a lab member, I want to be able to submit a request, register and edit equipment, and track them, so I can get what I	Thichanon	Partial	Y	Lab members can now edit their own request header, deadline, and details. The rest of the field can only be edited by the Lab manager and Admin.

	need for the lab.				
US-3	As a lab manager, I want to be able to view and assign lab requests to TAs.	Anawin, Thanathas, Hugo	Finished	Y	The lab manager can change a request status. A TA approved to work on a request can submit it for review
-	Backend code quality	Hugh, Thichanon	Finished	Y	Request API now passes pylint and mypy
-	Initialized Production deployment	Thanathas	In-Progress	Y	The docker-compose.prod.yml can run the website, but it still needs encrypting the ports and making reliability

3. Scope Addition/Change Log

Item added/changed	**Reason**	**What as dropped to compensate (one-in-one-out)**
Create Docker compose file for production	To prepare for the project deployment	-
Registration of the users from the admin on profile page	To give a way to the admin to create new users without using CLI	-
SRS-7 changed: TAs submit a request for review instead of escalating it to the lab manager	Escalating is not needed, the lab manager already assign TA and approve their ask	SRS-8 removed. closing is now done by the lab manager through status editing

4. Retrospective

What went well	What didn't go well	Action items for next sprint
Implementing really fast	Communication problems	Deployment of the App
We delivered SRS-1	Not splitting the work correctly and giving most of the work to only 2 people	Fix the problems and test our Application
-	Stacking pull request without accepting them	Handwritten Documentation documents (HW)

5. Testing & Quality Notes

The 7 tests in Iteration 5 were run.

Test run

Test	Test to perform	Result
SRS-1 File Uploading	Upload a valid file and confirm that it is attached to the correct record. Attempt uploads that exceed the configured size limit or use unsupported file types.	(Pass) Valid files upload successfully; invalid files are rejected with a clear message.
SRS-1 File downloading	Download an uploaded file using an authorized account, then attempt access using an account without permission.	(Pass) Authorised users can download the file, other users are refused
SRS-7 Submit request for review	As a TA approved to work on and in progress request, submit it for review. Then try the same as a TA who is not assigned to the request	(Pass) The approved TA moves the request to "Review" and the unassign TA is refuse
SRS-12 Equipment creation	Create equipment with valid details, then submit the form with required fields missing. Check the equipment list and detail page.	(Pass) Valid equipment is saved and displayed correctly; incomplete submissions show validation messages.
User creation	As the admin, create a user with	(Pass) Valid accounts are

	valid details. Test missing required fields and duplicate account details.	created with the selected role; invalid or duplicate details are rejected.
Create Docker compose file for production	Run “docker compose down -v”, then start with ‘prod.env’ and the prod compose files. Check “docker compose ps”, log in at http://localhost:3000 with the admin from ‘prod.env’, and try connecting to ports 3307 and 8000. Then remove ‘DB_PASS’ from prod.env and start again.	(Pass) Next runs next start and Flask runs Gunicorn. The admin can log in, and no demo accounts exist. Only port 3000 answers; 3307 and 8000 are refused. Without DB_PASS, startup stops and names the missing variable.
Activity history page	Perform actions that should create activity records, then open the activity history page and compare the entries with those actions. Check access permissions.	(Partial) Backend correctly logs all activity, frontend and views to fetch the logs are not implemented yet.

6. Project Risk Register

Risk ID	Description	Likelihood (L/M/H)	Impact (L/M/H)	Mitigation/ Contingency	Status
R-01	Stacking pull requests can lead up to merge conflicts	H	M	Coordinate changes and pull updates regularly. Resolve conflicts together and test before merging.	Open

R-02	Frontend and backend may use incompatible API formats, causing features to fail.	H	H	Agree on API formats and test integration early. Fix incompatible endpoints before release.	Open
R-03	A team member may be unavailable, delaying assigned tasks.	M	M	Share documentation and progress regularly. Reassign urgent tasks to available members.	Open

7. Individual Contribution Log

Student Name	Tasks owned this sprint	Course concept(s) applied	Evidence	Self-rated effort (1-5)

Thanathas Puttapipat	Create Docker compose file for production	MVP	Commit 6b049cc, 01f1fde, d9791bf	2.5/5
Anawin Chaichana	File attachment upload, restricting file access to users allow to see the request	CRUD, role-based access control	Commit 20e822c, 5da5dbc, 0a712b9, bc9681d	3.5/5
Hugh Jaiden	General fixes and backend for editing requests	CRUD, pair programming	Commit `f9c6894`, `4d49362`, `833fa36` (commit description)	3/5
Thichanon Kangkachit	New Equipment frontend + backend; Edit/Delete request and Equipment frontend	Modular Architecture	Commit ef4334f , 7b86381	3/5
Hugo Desvignes	File uploading (& downloading system) , User creation from admin profile page	CRUD , Front-end	Commit `f260a47` , `8591500`	3.5//5
