Course: Individual Software Development Process' 2026

Iteration Report: Iteration 4

By COOKIN'BYDOING

Chosen Irl Challenge: Project B: Lab Workflow & Request Management

Thanathas Puttapipat	6810545638
Anawin Chaichana	6810545964
Hugh Jaiden	6810546006
Thichanon Kangkachit	6810545611
Hugo Desvignes	6810546715


Table of Contents

1. Project Snapshot..... 3
2. Sprint/Board Status Snapshot.....**4**
3. Scope Addition/Change Log..... **5**
4. Retrospective..... **5**
5. Testing & Quality Notes.....**6**
6. Project Risk Register.....**7**
7. Individual Contribution Log..... **8**

1. Project Snapshot

Project Repository : https://github.com/0n0w1n/Vase_Lab_Management

Current Iteration Gantt Chart

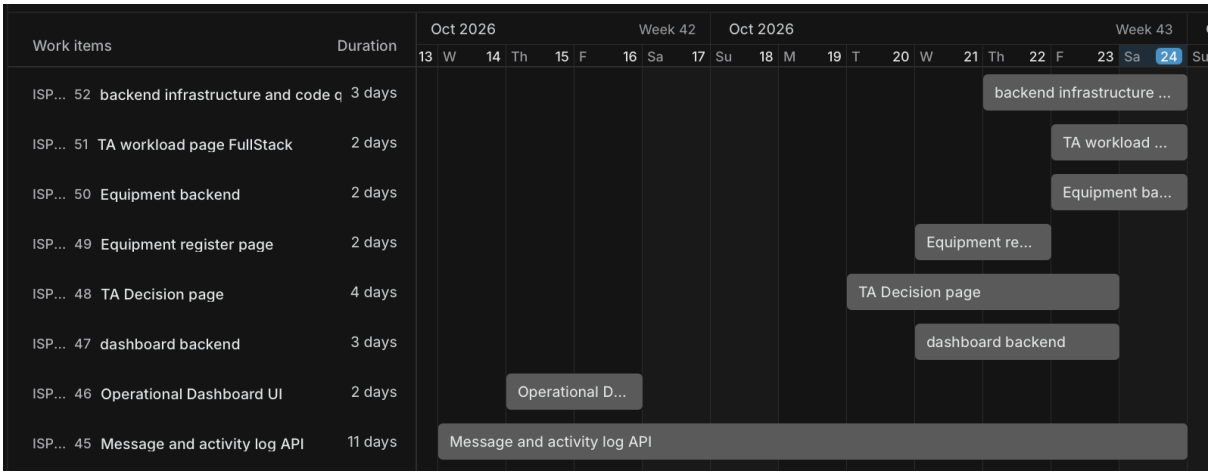

Critical Path:
Main Dashboard page → TA Decision → dashboard backend→ TA Workload → infrastructure fix
Critical Path Duration:
11 calendar days

2. Sprint/Board Status Snapshot

Iteration Goal: Let the lab manager oversee and assign requests. In this iteration we delivered the operational dashboard, the TA "WORK ON" request with the lab managers accept or denied decision and the TA workload view. We also add the first version of the equipment register and the message and activity log API

Capacity Declared: 3 user stories and 3 additional works. In Iteration 3 we finished 2 stories so we added one more story this time. We didn't count infrastructure as its own story. It maps to the story that depends on it.

User Story	Description	Owner	Status	Within Capacity (Y/N)	Notes
US-1	As a lab member, I want to be able to submit a request, register and edit equipment,	Anawin, Thichanon	Partial	Y	Only left for linking with the history log, and only SRS-1 is on hiatus due to possible implementing complications.

	and track them, so I can get what I need for the lab.				
US-2	As a TA, I want to see new requests submitted so I can request to work on it.	Anawin, Thanathas, Hugo	Finished	Y	TA can see new submitted requests and can ask for permission to work on it.
US-3	As a lab manager, I want to be able to view and assign lab requests to TAs.scrum	Anawin, Thanathas, Hugo	In-Progress	Y	Staff see all request and can filter by status and priority.SRS7 in iteration 4
-	As a lab managers want to see the efficiency of the TAs	Hugo	Finished	Y	Lab manager see the TA number of accepted request , the productivity can be easily seen
-	Activity history log	Hugh	In-Progress	Y	Backend is finished, all that's left is to connect it to the front end
-	Authorised Lab manager can edit request's TAs' capacity to work on	Thanathas	Finished	Y	Lab manager can increase or decrease the TAs' capacity to work on each request

3. Scope Addition/Change Log

Item added/changed	**Reason**	**What as dropped to compensate (one-in-one-out)**
Lab manager use dashboard to oversee requests	To help the lab manager to easily overlook what is happening in his lab system	-

Lab manager check workload page	Lab managers want to see the efficiency of the TAs	-
Lab manager can set TAs' capacity to work on	So that each request can have multiple TAs working on it	When a new request popped up the, lab manager has to always edit the capacity manually if the size is too limited.

4. Retrospective

What went well	What didn't go well	Action items for next sprint
Deliver more working features compared to previous iterations	Underestimating personal work load, leading to barely any activity in the first week of the iteration.	Attach a file to a request
Better overall project management organization	-	Review our code and check the security of our system
Connect every feature to each other	We still mainly merge without review (or with too little reviewers)	Make a document about our deployment choices (e.g :Hosting ; CI/CD ; FTP.....)

5. Testing & Quality Notes

The 10 tests in Iteration 4 were run.

Test run

Test	Test to perform	Result
SRS-11- Equipment page frontend	Go to the equipment page, check if it displays all equipment items and each item links to the dynamic page by a click.	(Pass) Displays all equipment and each one is linked to each dynamic page.
SRS-6	Lab manager assign or remove TA on the workload page or change request capacity	(Pass) The assignment is create or remove and log and capacity can not be set below the number of approve

SRS-6	TA or lab member calls the decision capacity or workload API directly	(Pass) Return 403 Unauthorized
SRS-6	lab manager approve or deny TA	(Pass) The receiving TA will be affected respectively by the lab manager's decision.
SRS-6	TA will not be able to ask for permission to work if the request's capacity is full	(Pass) If capacity is full, any other TA will no longer be able to press "Work on" it will instead show full
SRS-6	TA press "Work on" and send a message	(Pass) TA can presses "Work on" and adds message to the lab manager when checking in the "decisions" page
SRS-13	Lab manager open the operational dashboard	(Pass) Only lab manager can see the tab and access this page
SRS-13	TA or lab member try to open the dashboard	(Pass) They will not be able to see the dashboard on the side bar and not able to access the dashboard through the url
SRS-14	Dashboard show each request status, owner and priority and stay up to date	(Partial) Dashboard shows every request's status, owner, and priority and stays up to date, though the auto refresh still hasn't been implemented.
SRS-4, SRS-9, SRS-10	Confirm activity logs are created and in the correct format in the database	(Pass) All routes interacting with activity logs do not error, and the logs are correctly inserted when inspecting the database externally.

6. Project Risk Register

Risk ID	Description	Likelihood (L/M/H)	Impact (L/M/H)	Mitigation/ Contingency	Status
R-01	Having a merge conflict	H	L	Coordinate changes and pull updates regularly. Resolve conflicts together and test before merging.	Open
R-02	Users may modify other users' profiles without permission.	M	H	Check user identity and permissions in the backend before allowing updates. Test unauthorized requests	Closed
R-03	Frontend and backend may use incompatible API formats, causing features to fail.	M	H	Agree on API formats and test integration early. Fix incompatible endpoints before release.	Open
R-04	A team member may be unavailable, delaying assigned tasks.	M	M	Share documentation and progress regularly. Reassign urgent tasks to available members.	Open

7. Individual Contribution Log

Student Name	Tasks owned this sprint	Course concept(s) applied	Evidence	Self-rated effort (1-5)
Thanathas Puttapipat	Backend of the Dashboard page, Dashboard TA's decision page, and Request capacity adjustment feature	CRUD, MVP	Commit e8ba5df, f95bf01, 129978e, ca23fea,	5/5
Anawin Chaichana	Operational Dashboard UI, Equipment register backend	CRUD and modular architecture	commit f8795e2, 6ac07c0	4/5
Hugh Jaiden	Overseeing API modifications	CI, pair programming	Commit beb5e43, 16a21ad, b572c17, cb0932d	4/5
Thichanon Kangkachit	Equipment page and dynamic equipment page in frontend	Modular Architecture	Commit 316f8c8 , e9747c2	3/5
Hugo Desvignes	Link OP dashboard backend with front-end , full stack implementation of work load page for the op dashboard	CRUD , Design implementation	Commit `b050e0e`	3.75//5
