

Course: Individual Software Development Process' 2026

Iteration Report: Iteration 2

By **COOKIN'BYDOING**

Chosen Irl Challenge: Project B: Lab Workflow & Request Management

Thanathas Puttapipat	6810545638
Anawin Chaichana	6810545964
Hugh Jaiden	6810546006
Thichanon Kangkachit	6810545611
Hugo Desvignes	6810546715


Table of Contents

1. Project Snapshot.....	3
2. Sprint/Board Status Snapshot.....	4
3. Scope Addition/Change Log.....	5
4. Retrospective.....	5
5. Testing & Quality Notes.....	6
6. Project Risk Register.....	7
7. Individual Contribution Log.....	8

1. Project Snapshot

Project Repository : https://github.com/0n0w1n/Vase_Lab_Management

Current Iteration Gantt Chart

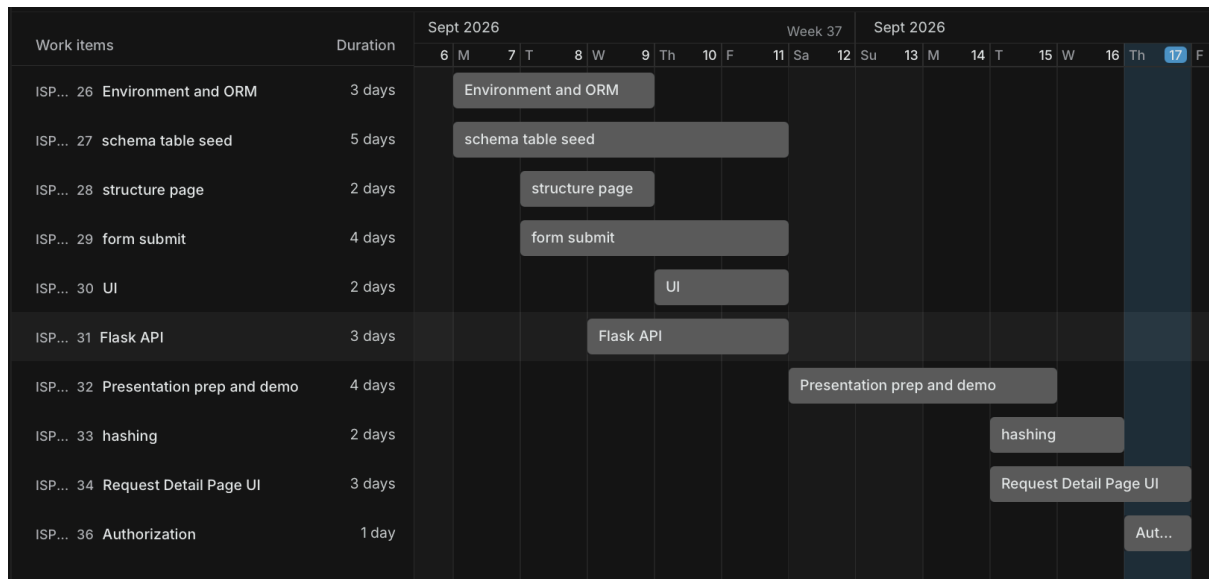

Critical Path: Request/user/status schema implemented in the ORM then Flask. Switched from mock data to the Flask API user-table correction and password hashing then authorization but not apply to web yet

Critical Path Duration: 11 calendar days

2. Sprint/Board Status Snapshot

Iteration Goal: Deliver the submit → save → display, then authentication so that requests are attributed to, and filtered by, the signed-in user. Supports Sub-Goals SG-1 and SG-2. This was achieved in the first half of the iteration and demonstrated at the mid-term checkpoint; authentication was taken up immediately afterward. Authentication is partially delivered and the web application does not call the login API yet

Capacity Declared: 2 user stories. Authentication is not declared as a separate story, it is mapped onto US-1 and US-3, both of which depend on it, rather than a user-facing scope of its own.

User Story	Description	Owner	Status	Within Capacity (Y/N)	Notes
US-1	As a lab member, I want to submit a request and track it, so I can get what I need for the lab	Anawin Chaichana	In-Progress	Y	SRS-2 and SRS-3 delivered and tested. and a valid request is saved with a unique ID and status "Pending", together with its activity-log. SRS-4 delivered in partial. Equipment register/edit remains deferred to a later iteration as it belongs to SG-4.
US-3	As a lab manager, I want to be able to view and assign lab requests to TAs	Thichanon Kangkachit	In-Progress	Y	Reads live data through the Flask API. Assignment and status-change logic (SRS-6) and the TA escalation path (SRS-7) remain deferred, as no endpoint yet writes a status change

3. Scope Addition/Change Log

Item added/changed	Reason	What as dropped to compensate (one-in-one-out)
Request type field remove	It's not that useful for our work if theres request that doesn't fit the provide type	-

4. Retrospective

What went well	What didn't go well	Action items for next sprint
Iteration 1 action item was met, a working submit, save, display was delivered.	The database and the interface used different status words, found when the two halves were connected. Fixing it late meant changing the model, migration, seed, types and two components at once.	Agree names between backend and frontend owners before it is written.
Work was split, so no two members duplicated a component.	Some contributions were overwritten because members worked in overlapping areas without saying so.	Commit and push at the end of each session, and state in the group channel what area you are working in before starting.
Capacity was declared from measured time rather than estimate.	A migration was edited in place, forcing everyone to rebuild their local database.	Announce changes that break other members environments before they land.

5. Testing & Quality Notes

The three tests declared in Iteration 1 were run.

Test run

Test	Test to perform	Result
SRS-2	Validation error shown request not saved	Pass. 400 returned with an errorCode and a single error description; no row written
SRS-3	Saved with a unique request ID and status "Pending"	Pass. 201 returned with the new ID, and the activity-log entry written in the same transaction
SRS-4	Only that member's own requests listed, with current status	Partial. The list reads live data and shows current status, but is not filtered per user.
Flask endpoint	All endpoints respond correctly	Pass. List 200, detail 200, unknown ID 404, invalid input 400
TypeScript	No errors	Pass. The status components are typed against the status list, which is how every place needing the new values was found
SRS-10	Log in with valid account	Pass. JWT access token returned
SRS-10	Log in with a wrong password or unknown email	Pass. Both return 401 with the same message, so accounts cannot be enumerated

6. Project Risk Register

Risk ID	Description	Likelihood (L/M/H)	Impact (L/M/H)	Mitigation/Contingency	Status
R-01	No runnable build in Iteration 1, so schema and validation defects stay undetected	H	M	Delivered the submit, save, display path	Closed
R-02	Schema, interface and container stack were built in parallel and not yet integrated	M	H	All three integrated on the shared Compose stack before authentication work began	Closed
R-03	Only Hugh Jaiden can run and configure Docker, a single point of failure for the whole team	M	H	Other members now bring the stack up independently.	Closed
R-04	No velocity baseline, so Iteration 2 capacity may be over-declared	M	M	Capacity declared from measured time per item. held at 2 stories rather than increased	Closed
R-05	Files are mounted at runtime rather than copied at build time, so the development container does not match a clean build; deployment may fail on issues not visible during development	M	M	A build-based configuration is still to be verified before deployment	Open

7. Individual Contribution Log

Student Name	Tasks owned this sprint	Course concept(s) applied	Evidence	Self-rated effort (1-5)
Thanathas Puttapipat	New Request form. dynamic route for the new-request page. Design UI and recheck UI	Follow KAOS goal modeling by directing the team's attention to implement request management features instead of authorisation.	Commit : "ed402b7", "3a47506" Figma	4
Anawin Chaichana	Login page UI. Connecting requests page to database.make frontend work with rework api	Database transactions and data integrity.	Commits : "817dc82", "c4ba6b2", "9e4c46c"	4
Hugh Jaiden	API rework and JWT authentication	Security	Commits : "ee2abf8", "8aedacc", "57f8421"	4
Thichanon Kangkachit	Apply the new dynamic request layout and fix the navigation for dynamic request	Modular architecture	Commits : "3a47506"	4
Hugo Desvignes	ORM implementation.; user-table schema correction and Argon2 password hashing	ORM mapping. PK FK connect table	Commits : "d41dd6d", "1a34d5d", "b9a3e35"	5
